











ID	Task Name	Duration	Start	Jun 4, '06							Jun 11, '06							Jun 18, '06	
				S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M
1	<b>Client Presentation Phase</b>	<b>8 days?</b>	<b>Mon 6/5/06</b>																
2	Client Appliance Selection times	6 days	Mon 6/5/06																
3	Client Plumbing and Lighting Selection times	8 days	Mon 6/5/06																
4	Initial measure 4hrs	1 day?	Mon 6/5/06																
5	Design Measure	1 day?	Mon 6/5/06																
6	Set Site visit w/ Subs	0 days	Mon 6/5/06																
7	Existing Floor plan 3-6 hrs	1 day?	Tue 6/6/06																
8	Design time	2 days	Wed 6/7/06																
9	Site study, bulk plane req, site plan 2-6 hrs	1 day?	Thu 6/8/06																
10	Preliminary Design Schemes w/ 3D 5-12 hrs	2 days	Fri 6/9/06																
11	Client Design Review 3-3hrs	2 days	Tue 6/13/06																
12	Design Sales meeting	2 days	Tue 6/13/06																
13	<b>Sub Estimate Phase</b>	<b>14 days?</b>	<b>Tue 6/13/06</b>																
14	Structural Prelim	1 day?	Tue 6/13/06																
15	Mechaincal Plan 1 hrs	1 day?	Tue 6/13/06																
16	Plumbing Plan 1hr	1 day?	Tue 6/13/06																
17	Electrical Plan 2hrs	1 day?	Wed 6/14/06																
18	Sub Contractor site meeting / pricing	12 days	Thu 6/15/06																
19	Engineer Site Visit	1 day?	Thu 6/15/06																
20	Design Sales Pricing	4 days	Thu 6/15/06																
21	<b>Client Construction Intent Phase</b>	<b>4 days?</b>	<b>Fri 6/16/06</b>																
22	Final Design Schemes 2-8hrs	1 day	Fri 6/16/06																
23	Cabinet Plans 2-6 hrs	1 day?	Mon 6/19/06																
24	Exterior Elevations 4-8 hrs	1 day?	Tue 6/20/06																
25	Client price & design review	1 day?	Wed 6/21/06																
26	Sales Design Meeting	1 day?	Wed 6/21/06																
27	Revisions price and Plan 2-4 hrs	3 days	Thu 6/22/06																
28	2nd Client price & design review	1 day?	Tue 6/27/06																
29	Sales Design Meeting	1 day?	Tue 6/27/06																
30	<b>City Plan Review Phase</b>	<b>25 days?</b>	<b>Wed 6/21/06</b>																
31	Plot Plan	1 day?	Wed 6/21/06																








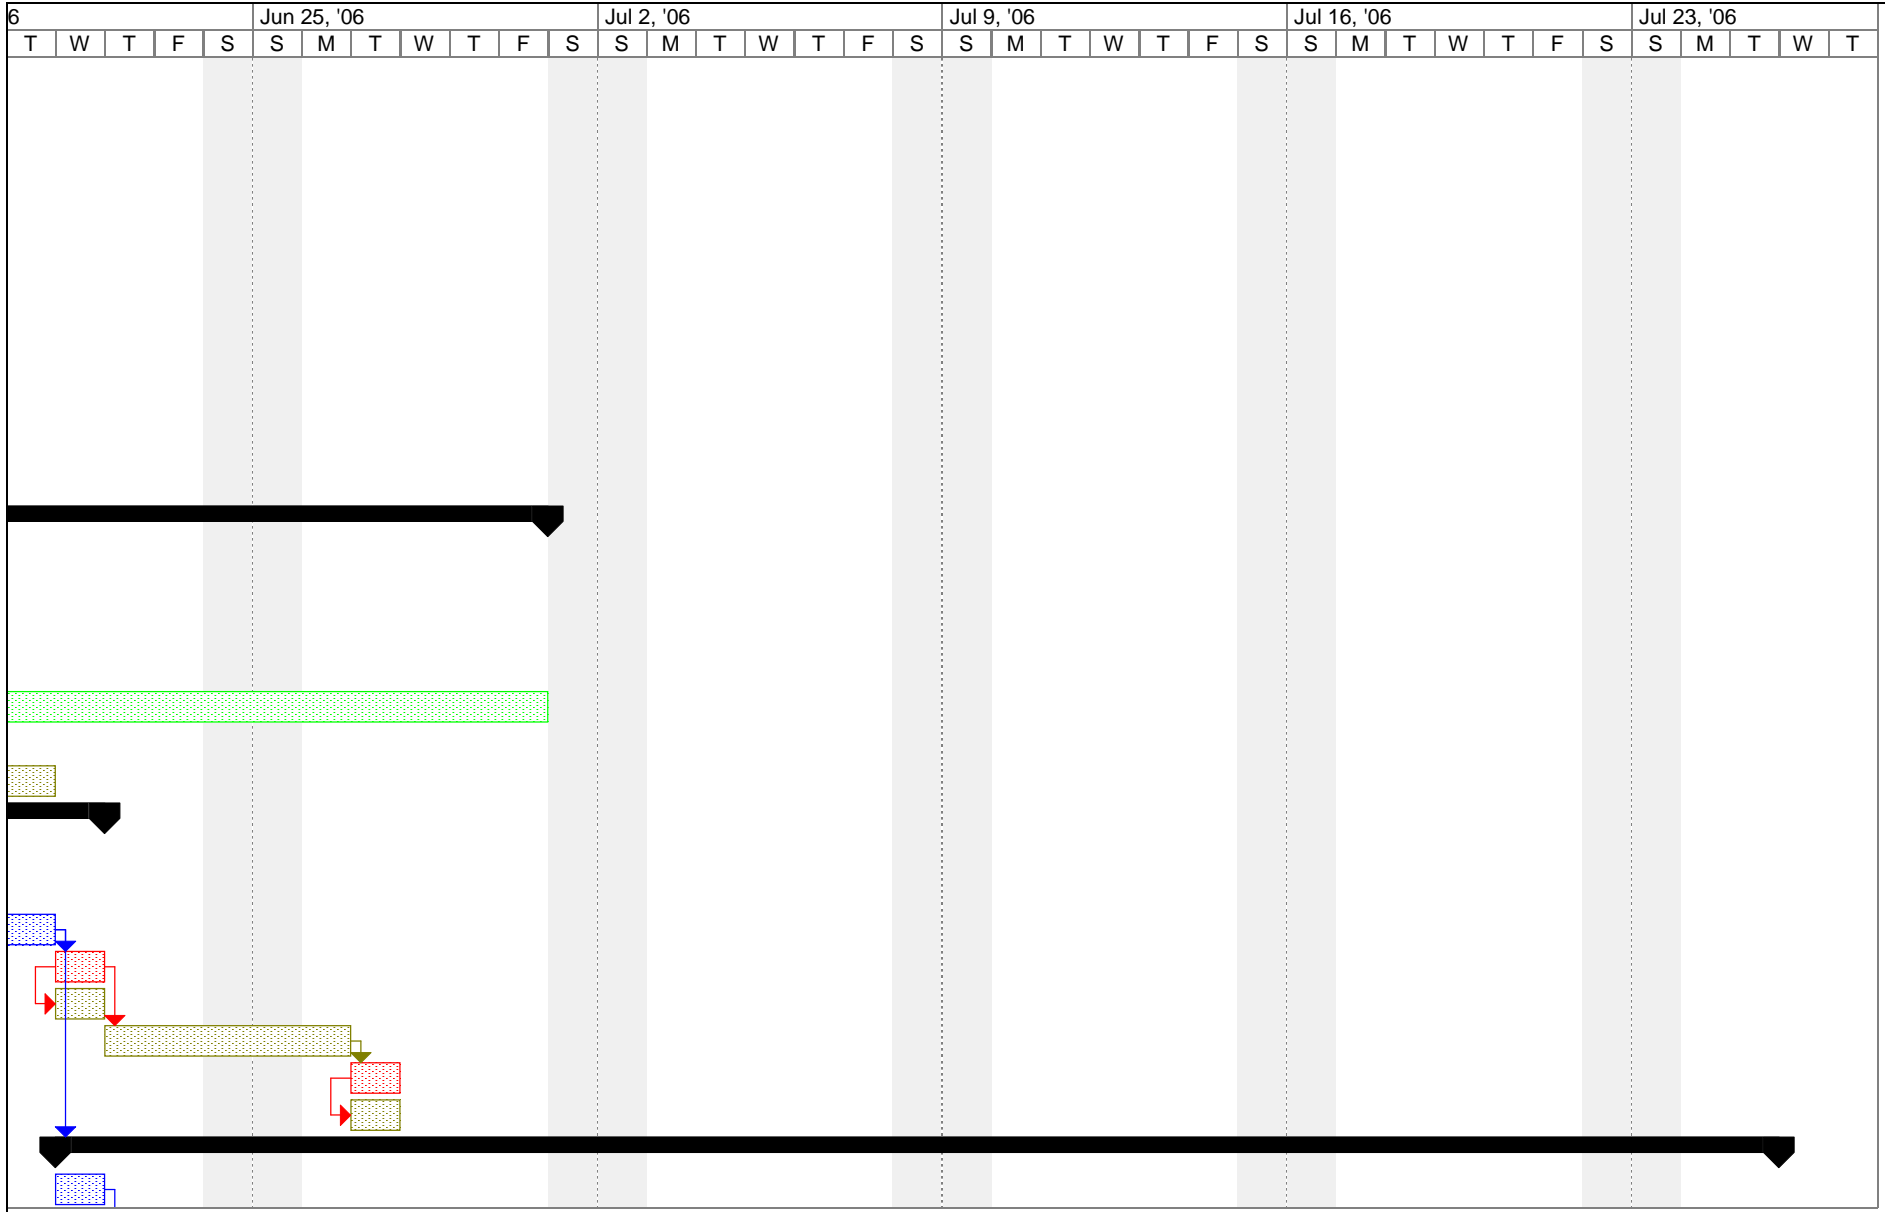

Project: Sample Drw completion timeli Date: Wed 12/29/10	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	


ID	Task Name	Duration	Start	Jun 4, '06							Jun 11, '06							Jun 18, '06		
				S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	
32	Revised Floor Plans	1 day?	Thu 6/22/06																	
33	Framing Plans	1 day?	Fri 6/23/06																	
34	Framing Section & Details	1 day?	Mon 6/26/06																	
35	Structural Plans, Foundation, roof etc.	1 day?	Mon 6/26/06																	
36	Mech Plans Revised	1 day?	Tue 6/27/06																	
37	Plubing Plans Revised	1 day?	Tue 6/27/06																	
38	Electrical Plans Revised	1 day?	Tue 6/27/06																	
39	City Review	20 days?	Wed 6/28/06																	
40	<b>Client Contract Signing Phase</b>	<b>7 days?</b>	<b>Wed 6/28/06</b>																	
41	Cabinet Elevations & Hardware schedule	1 day?	Wed 6/28/06																	
42	Cabinet Perspective / Rendering	1 day?	Thu 6/29/06																	
43	Door, Window & Glass Schedule	1 day?	Fri 6/30/06																	
44	Room Finish Schedule	1 day?	Mon 7/3/06																	
45	Tile Plans, Elevations & Details	1 day?	Tue 7/4/06																	
46	Staging Plan	1 day?	Wed 7/5/06																	
47	Client Agreement Sign-Off	1 day?	Thu 7/6/06																	
48	Sales Deigne Meeting	1 day?	Thu 7/6/06																	
49	<b>Internal Construction Document Completion Phase</b>	<b>14 days?</b>	<b>Fri 7/7/06</b>																	
50	Demolition plan	2-4 hrs	1 day?																	
51	General Notes	2-8 hrs	2 days																	
52	Cabinet order Plans and Elevations 4		3 days																	
53	Int Trim & Section views	4-8 hrs	3 days																	
54	Plumbing elevations	3-6	1 day?																	
55	Elec. Elevations	3-6 hrs	1 day?																	
56	Electrical Reflected Celing plans	1-2 hrs	1 day?																	
57	Elec Appliance Specs	2-3 hrs	1 day?																	
58	Shop Drawing cabs, tops, mirros, etc.	5-10 hrs	3 days																	

Project: Sample Drw completion timeli Date: Wed 12/29/10	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	








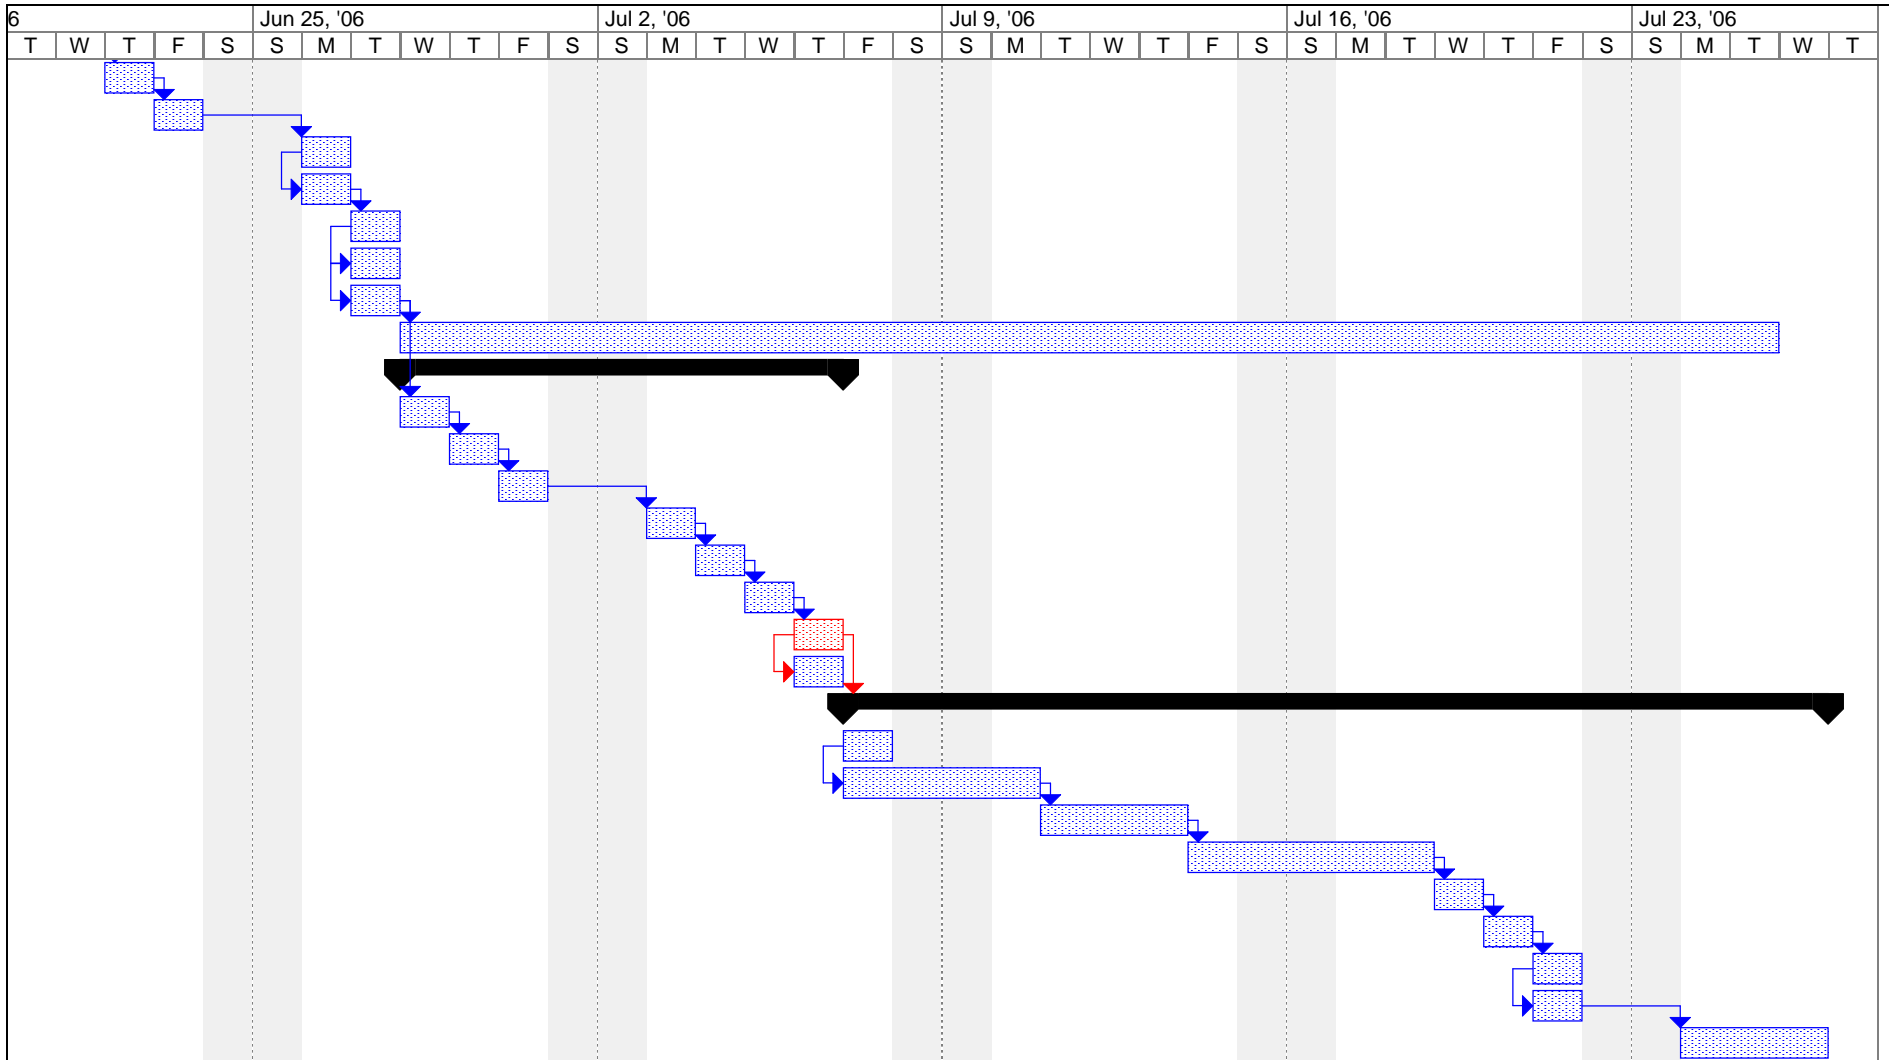


Project: Sample Drw completion timeli  
 Date: Wed 12/29/10

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	



Project: Sample Drw completion timeli  
 Date: Wed 12/29/10

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
